Gainesville - Hall Metropolitan Planning Organization (GHMPO)
Hall County, Georgia

Spout Springs Road Widening Project

ID	Task Name	% Complete	Duration	Start	Finish
1	**Spout Springs Road Widening Project**	**0%**	**871 days**	**Thu 10/22/09**	**Thu 2/21/13**
2	Notice to Proceed	100%	1 day	Thu 10/22/09	**Thu 10/22/09**
3	**Design Phase**	**0%**	**210 days**	**Fri 10/23/09**	**Thu 8/12/10**
4	Utility Locate	0%	1 mon	Fri 10/23/09	Thu 11/19/09
5	Survey	0%	1 mon	Fri 10/23/09	Thu 11/19/09
6	Concept Design	0%	2 mons	Fri 10/23/09	Thu 12/17/09
7	**Concept Design Submittal**	0%	0 days	Thu 12/17/09	Thu 12/17/09
8	Const. Plans - 30%	0%	2 mons	Fri 12/18/09	Thu 2/11/10
9	**30% Plan Submittal**	0%	0 days	Thu 2/11/10	Thu 2/11/10
10	Const. Plans - 60%	0%	2 mons	Fri 2/12/10	Thu 4/8/10
11	**60% Plan Submittal**	0%	0 days	Thu 4/8/10	Thu 4/8/10
12	Const. Plans - 90%	0%	2 mons	Fri 4/9/10	Thu 6/3/10
13	**90% Plan Submittal**	0%	0 days	Thu 6/3/10	Thu 6/3/10
14	Const. Plans - 100%	0%	1 mon	Fri 6/4/10	Thu 7/1/10
15	**100% Plan Submittal**	0%	0 days	Thu 7/1/10	Thu 7/1/10
16	Plan Submittal for Regulator Review	0%	30 days	Fri 7/2/10	Thu 8/12/10
17	**Regulatory Approval**	**0%**	**120 days**	**Fri 2/12/10**	**Thu 7/29/10**
18	NEPA Preperation	0%	2 mons	Fri 2/12/10	Thu 4/8/10
19	NEPA Submittal	0%	0 days	Thu 4/8/10	Thu 4/8/10
20	Regulatory Review	0%	4 mons	Fri 4/9/10	Thu 7/29/10
21	NEPA Approval	0%	0 days	Thu 7/29/10	Thu 7/29/10
22	**Right of Way Plans Phase**	0%	2 mons	Fri 2/12/10	Thu 4/8/10
23	**Right of Way Acquisition Phase**	**0%**	**260 days**	**Fri 4/9/10**	**Thu 4/7/11**
24	Appraisals	0%	6 mons	Fri 4/9/10	Thu 9/23/10
25	Appraisal Review	0%	6 mons	Fri 5/14/10	Thu 10/28/10
26	Negotiation	0%	9 mons	Fri 6/18/10	Thu 2/24/11
27	Condemnation	0%	9 mons	Fri 7/16/10	Thu 3/24/11
28	Closings	0%	9 mons	Fri 7/30/10	Thu 4/7/11
29	**Construction Phase**	**0%**	**24 mons**	**Fri 4/22/11**	**Thu 2/21/13**

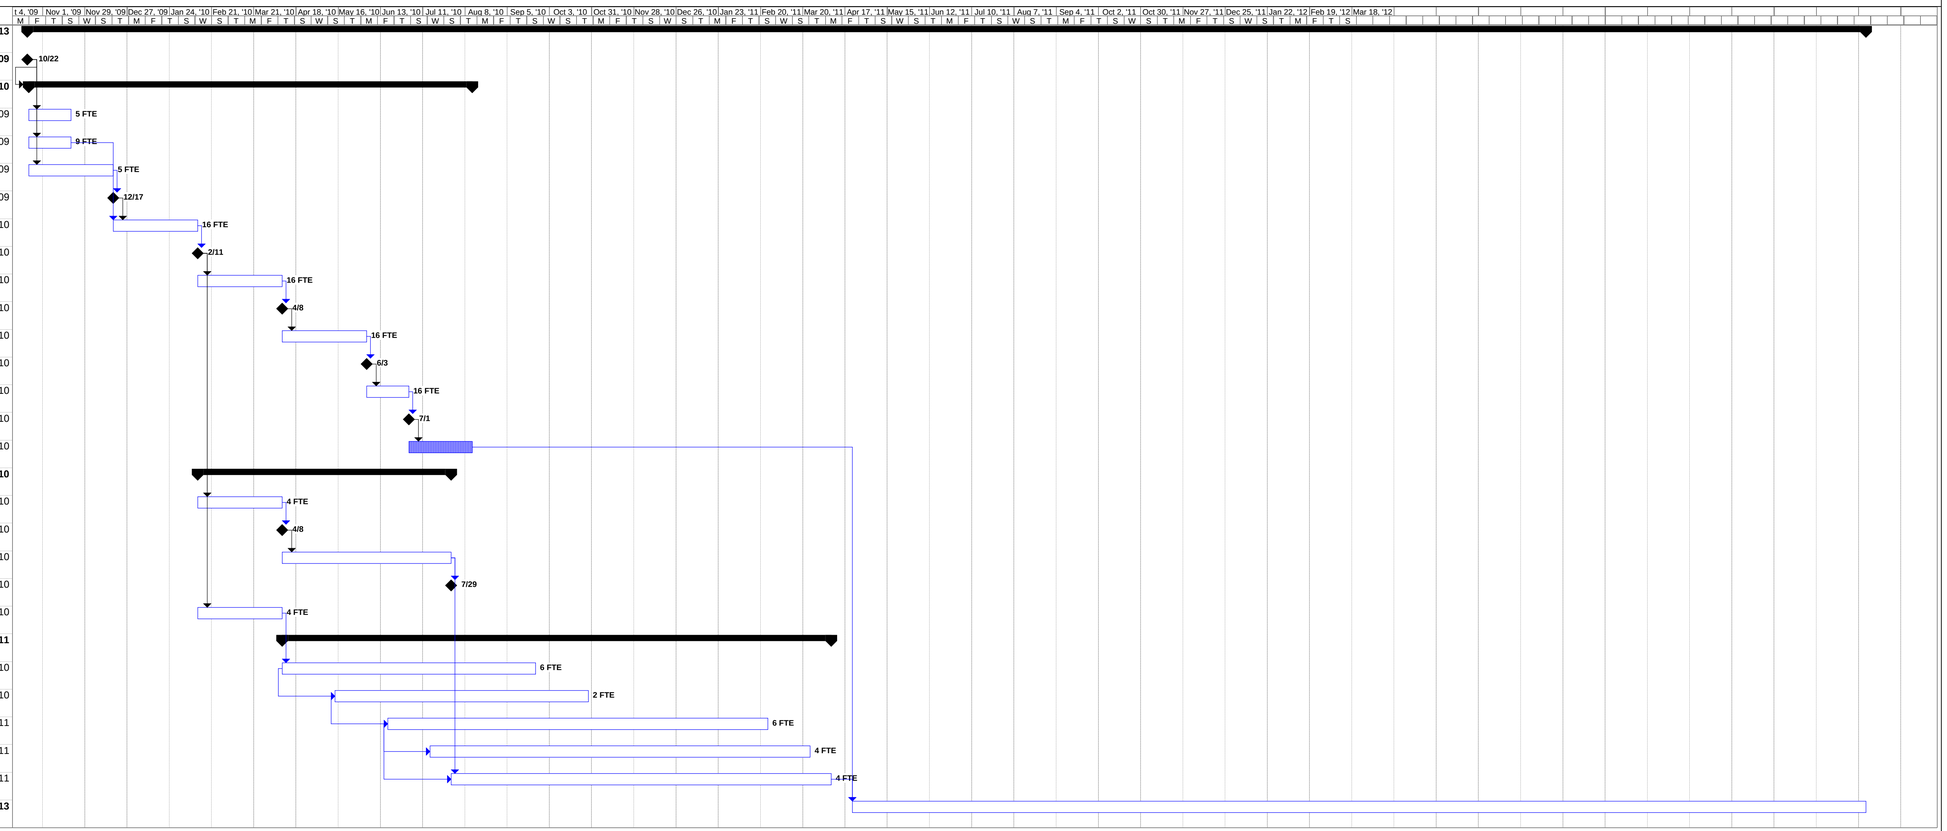

Project: Spout Springs Road Widening
Date: Mon 9/14/09

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
